



Wanganui District Council

Building a better community with the people of the Wanganui District

Fill in all relevant details. Attach two (2) copies of all documents

PLEASE TICK APPROPRIATE BOX

This application is for a:

- ☐ BUILDING CONSENT
☐ PROJECT INFORMATION MEMORANDUM (P.I.M)
☐ BUILDING CONSENT AS PER P.I.M No. _____

OWNER

Name: Mrs Nyma
 Mailing Address: 45 Lewis Ave
Wanganui Ph: 3432715

PROJECT

Description of Project and Use: _____
Install P100 FreeStanding Fire

CONTACT PERSON

Neville Elmer
 Phone: 3455891 Fax: 3453941

INTENDED LIFE OF PROJECT

- ☐ Indefinite, but not less than 50 years
☐ Other - specified as: 7 years

VALUE

Value: \$ 2000.00 (Incl. G.S.T)

PROJECT LOCATION

Street Address/Rural No.: _____
45 Lewis Ave

NEW RESIDENTIAL DWELLINGS OR NEW COMMERCIAL ONLY

Floor Area: _____ M²

Office use only

LEGAL DESCRIPTION

Property Number: 10405
 Valuation Roll Number: _____
 Lot(s): _____ DP: _____ Section: _____
 Block: _____ Survey District: _____

KEY PERSONNEL

Consent fees to be paid by: _____
 Builder(s): _____
 Registered Drainlayer: _____
 Registered Plumber: _____
 Building Certifier: _____

Palmer's Plumbing & Heating Ltd
 293 VICTORIA AVENUE
 WANGANUI
 PH: (06) 3455891 Fax: (06) 3453941

FEES APPLICABLE

BUILDING CONSENT	\$	_____
P.I.M	\$	_____
NON NOTIFIED APP. FEE	\$	_____
PREPAID CROSSING	\$	_____
PREPAID SEWER CONNECTION	\$	_____
PREPAID WATER CONNECTION	\$	_____
STORMWATER CONNECTION	\$	_____
DRAINAGE LEVY	\$	_____
DEVELOPMENT LEVY	\$	_____
BUILDING RESEARCH LEVY	\$	_____
BIA LEVY	\$	_____
TOTAL FEES (Incl. G.S.T)	\$	<u>50.00</u> paid

Signed by or for and on behalf of the applicant:

Signature: M. Elmer

owner, builder, plumber, designer, agent
(circle appropriate one)

Date: 27-10-94

PART B: PROJECT DETAILS (omit if a PIM has been applied for separately)

The project involves: (tick each applicable box, if any, and attach relevant information in duplicate).

- (1) ☐ Location in relation to legal boundaries, and external dimensions of new, relocated, or altered buildings.
- (2) ☐ New provisions to be made for vehicular access and on-site parking, ie: new crossing.
- (3) ☐ Provisions to be made in building over or adjacent to any road or public place, ie: hoardings, signs.
- (4) ☐ New provisions to be made for disposing of stormwater and wastewater.
- (5) ☐ Precautions to be taken where building work is to take place over existing drains or sewers or in close proximity to wells or watermains.
- (6) ☐ New connections to public utilities, ie: new drainage or water connections.
- (7) ☐ Provisions to be made for any demolition work, ie: the protection of the public, suppression of dust, disposal of debris, disconnection from public utilities and suppression of noise.
- (8) ☐ Any cultural heritage significance of the building or building site, including whether it is on a marae.

PART C: PROJECT DETAILS (complete in all cases)

Documents provided with this application:

- ☐ Plans and specifications
- (21) ☐ Producer Statements (ie: design certificate, design review, truss certificates, etc)
- (22) ☐ Other documents (ie: accreditations, etc)

Inspections proposed:

- (26) ☐ By W.D.C
- (27) ☐ Other - specify (ie: Design engineer, etc)

for office use only													
DEPT.	CHECKS					INSPECTIONS			ADTNL CHGS		P.W.R	APPROVED	
	INITIALS	DATE	INITIALS	DATE	TIME	NO.	TIME	TOTAL	TYPE	AMOUNT	NO.	INITIALS	DATE
ADMINISTRATION	<i>[Signature]</i>	2/1/00											
PLANNING													
BUILDING	<i>[Signature]</i>	2/1/00			5	1	30	30				<i>[Signature]</i>	2/1/00
DRAINAGE ENGINEER													
WATER ENGINEER													
STRUCTURAL ENGINEER													
PLUMBING & DRAINAGE													
TRAFFIC ENGINEER													
HEALTH													
DANGEROUS GOODS													
Totals	Total check time (minutes)					Total (min)					Total \$		
Approved for issue of PIM/Building Consent											G.S.T \$		
District Building Controller: <i>[Signature]</i>											Date: 28/OCT/1994		
											TOTAL \$		

Mrs. Rymer
45 Lewis Ave
Wingate

Magnum P100 Fire
on Tile Hearth

Lounge

Dining

Kitchen

MAGNUM WARRANTY

CASTWORKS warrants the Cast Iron Firebox of your magnum stove against faulty parts and workmanship for five years from date of initial purchase. All other parts including baffle, firebox liners, door and cabinet, are warranted for twelve months from initial purchase date.

WARRANTY CONDITIONS

1. The heater must be installed and operated strictly according to the Installation and Operation Manual.
2. The warranty covers the replacement or repair at the manufacturers discretion, of any component part of the stove found to be defective due to faulty materials or workmanship.
3. The manufacturer, CASTWORKS, or the local distributor is not liable for any loss or expense — direct or indirect — arising from the failure of any part or operation of the stove.
4. Freight and/or travelling expenses are excluded from this warranty.

IMPORTANT — The following should be completed at time of purchase and retained by the owner.

PURCHASER'S NAME.....

ADDRESS.....

DEALER NAME.....


ADDRESS.....

PURCHASE DATE..... SERIAL NUMBER.....

MODEL..... COLOUR.....

LOCAL CONSUMER LAWS APPLY TO THIS WARRANTY

INSTALLATION AND OPERATION MANUAL

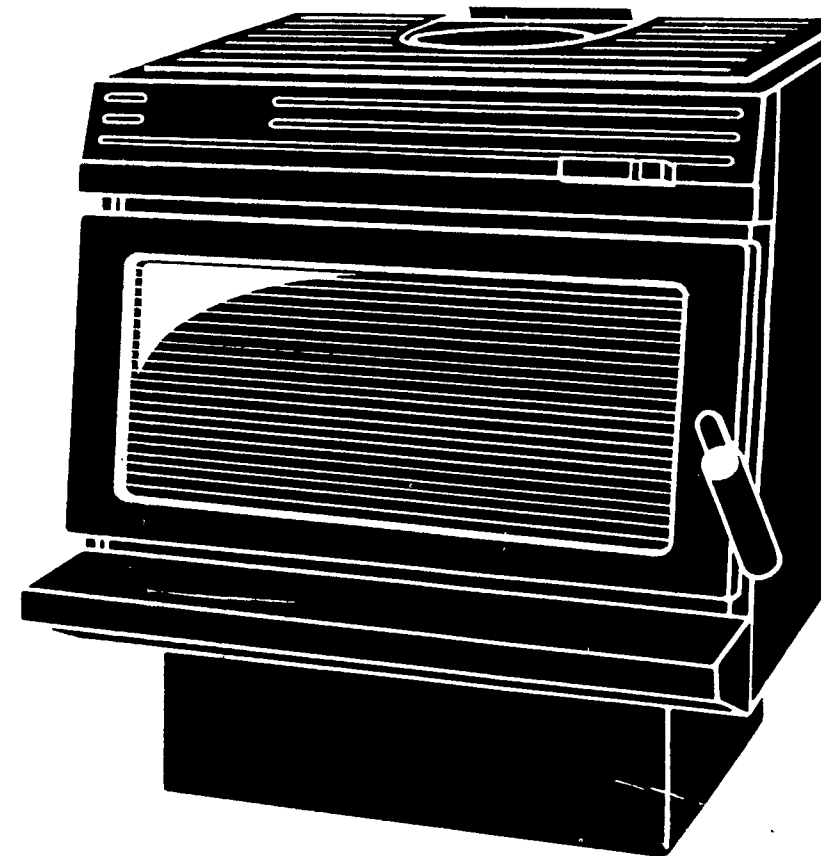

MAGNUM[®]

© Registered trademarks of: ROBERT MONG LIMITED, P.O. Box 7068 Fitzroy, New Plymouth, New Zealand, Phone (06) 755 0209, Fax (06) 755 1435

A **CASTWORKS**[®] PRODUCT

MAGNUM[®]
P-100

INSTALLATION

As building and safety requirements for wood burning stove installations vary, check with your local building inspector prior to commencing installation. A permit may be required. It is recommended your Magnum stove be installed by a registered plumber or specialist suitably qualified in the installation of free-standing fireplaces.

FLUE:

We recommend you purchase a double cased, matt, vitreous enamel flue kit for your Magnum woodstove. A minimum 3.6 metre length of 150mm diameter fluepipe is required.

HEARTH:

The following hearth specifications comply with the standards as shown:

MAGNUM P100 - NZS 7421 Does not require an insulating hearth but must have an ash hearth extend horizontally 200 mm in all directions vertically below the door opening.	MAGNUM P100 - AS 2918 Does not require an insulating hearth but must have an ash hearth extend horizontally 300mm forward of the door opening and 200mm to each side of the door opening.
--	---

Provision is made at the rear of the pedestal for seismic restraint by bolting through the two holes as showing on the assembly diagram.

WALL CLEARANCES:

Your Magnum stove may be installed with minimal clearances from a combustible wall but may require a flue heat shield to be fitted. (Refer chart below):-

Without Flueshield	Rear clearance	400mm
	Side clearance	300mm
	Corner clearance	295mm
With Single Flueshield	Rear clearance	200mm
	Side clearance	250mm
	Corner clearance	95mm
With Magnum Double Flueshield	Rear clearance	50mm
	Side clearance	250mm
	Corner clearance	50mm

WATER BOOSTER

To fit the water booster proceed as follows:-


- Remove the rear panel.
- Remove the pre-punched knockouts from both the rear panel and inner rear heat shield (5 on inner panel and 2 on rear panel).

- Remove the blanking plugs fitted to the rear casting of the firebox, accessible through the 2 large knockouts just removed.

- Remove the 3 bolts and nuts fitted to the rear firebox casting, accessible through the 3 x smaller knockouts just removed.

- Fit the water booster into the firebox as illustrated opposite.

- Secure the water booster casting to the rear of the firebox utilising the 3 nuts and bolts (previously removed in D. above). Fit bolts from inside firebox.

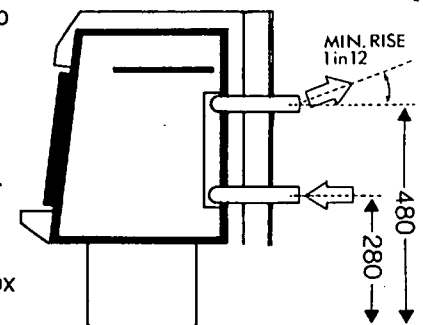

NOTE

- The water booster can only be connected to a low pressure vented system.
- The distance between heater and hot water storage cylinder should be kept to a minimum and not exceed four metres.
- A minimum rise of 1 in 12 is recommended for the hot return pipe.

OPERATION

Your Magnum should be "run in" as with a new car, gradually working it up to operating temperature. Begin with a few small fires progressively building up to a full sized load. Allow the heater to cool thoroughly between each fire.

Do not remove the ashes, allowing them to build up.

Place a quantity of paper or fire lighters into the firebox as starter material and add dry kindling. Open the air control fully, light the starter material and close the door. Once the fire is well alight add larger pieces of timber until you have a well established fire.

The Magnum P100 air control should be operated in the LOW to HIGH range. As a safety feature, in the unlikely event of a flue fire, lift the air control knob slightly and move it fully to the right to the OFF position.

THESE FOLLOWING POINTS ARE MOST IMPORTANT:

- The stove will give off an odour and fumes during the initial firing. Do not be alarmed, this is the firebox paint curing and will continue for approximately 15-30 minutes.
- Do not burn wet timber or chemically treated timber as this causes flue blockage, has low heat output and blackens the door glass. Burn dry seasoned timber and remember:-
 - The dryer the wood the hotter it burns
 - The harder the wood the longer it burns
- Always keep a layer of ash (approximately 15mm) in the firebox. This acts as an insulator and improves combustion and efficiency.

INSTALLATION - NOT TO BE USED
